Nr.	Event	Duration	Start	End	Precursor
1	**NAR-Discussion**	**155 t**	**03.01.2005**	**05.08.2005**	
2	NSTR-discuss + model doc	95 t	03.01.2005	13.05.2005	
3	NSTR model doc approval phase	18 t	16.05.2005	08.06.2005	2
4	NMAN-discuss + model doc	95 t	03.01.2005	13.05.2005	
5	NMAN model doc approval phase	18 t	16.05.2005	08.06.2005	4
6	NMDF-discuss + model doc	95 t	03.01.2005	13.05.2005	
7	NMDF model doc approval phase	18 t	16.05.2005	08.06.2005	6
8	CoCo-discuss + model doc	95 t	03.01.2005	13.05.2005	
9	CoCo model doc approval phase	18 t	16.05.2005	08.06.2005	8
10	CoCo individual comp discuss + spec	4 M	18.04.2005	05.08.2005	
11	ArchImplGuidelines - discuss + delivery	95 t	03.01.2005	13.05.2005	
12	NAR model (STA) approved	0 t	08.06.2005	08.06.2005	3;5;7;9;11
13	**NAR-Implementation**	**100 t**	**09.06.2005**	**26.10.2005**	
14	NMDF model impl work + tech docs	3 M	09.06.2005	31.08.2005	7;12
15	NMDF implementation approval	18 t	03.10.2005	26.10.2005	14
16	NAR structure impl discussion	1 M	09.06.2005	06.07.2005	3;5;11;12
17	NAR structure impl work + tech docs	1 M	01.09.2005	28.09.2005	14;16
18	NAR implementation approval phase	18 t	03.10.2005	26.10.2005	17
19	NAR-Implementation completed	0 t	26.10.2005	26.10.2005	18
20	**CoCo implementation**	**10 t**	**27.10.2005**	**09.11.2005**	
21	Labels comp spec	2 W	27.10.2005	09.11.2005	12;18;19
22	Description comp spec	2 W	27.10.2005	09.11.2005	18;12;19
23	Signature comp spec	2 W	27.10.2005	09.11.2005	18;12;19
24	Rights comp spec	2 W	27.10.2005	09.11.2005	18;12;19
25	etc comp spec	2 W	27.10.2005	09.11.2005	18;12;19
26	**NewsML2-Discussion**	**120 t**	**09.06.2005**	**23.11.2005**	
27	Requirements doc	2 M	09.06.2005	03.08.2005	12
28	Model doc	1 M	13.10.2005	09.11.2005	27;20EE
29	Requ + model approval	10 t	10.11.2005	23.11.2005	27;28
30	**NewsML2-Implementation**	**141 t**	**24.11.2005**	**08.06.2006**	
31	tech implementation	2 M	24.11.2005	18.01.2006	29;19
32	testing + tech doc	1 M	19.01.2006	15.02.2006	31
33	approval phase	18 t	21.02.2006	16.03.2006	32
34	STA approval	0 t	16.03.2006	16.03.2006	33
35	full doc + examples + tutorials	3 M	17.03.2006	08.06.2006	34
36	Ready for ROLL OUT	0 t	08.06.2006	08.06.2006	35
37	**EventsML-Discussion**	**120 t**	**09.06.2005**	**23.11.2005**	
38	Requirements doc	2 M	09.06.2005	03.08.2005	12
39	Model doc	1 M	13.10.2005	09.11.2005	38;20EE
40	Requ + model approval	10 t	10.11.2005	23.11.2005	39;38
41	**EventsML-Implementation**	**141 t**	**24.11.2005**	**08.06.2006**	
42	tech implementation	2 M	24.11.2005	18.01.2006	40;19
43	testing + doc	1 M	19.01.2006	15.02.2006	42
44	approval phase	18 t	21.02.2006	16.03.2006	43
45	STA approval	0 t	16.03.2006	16.03.2006	44
46	full doc + examples + tutorials	3 M	17.03.2006	08.06.2006	45
47	Ready for ROLL OUT	0 t	08.06.2006	08.06.2006	46
48	**SportsML (to be discussed)**	**120 t**	**09.06.2005**	**23.11.2005**	
49	NAR compliant version: spec + impl	6 M	09.06.2005	23.11.2005	12
50	AGM 2006	0 t	05.07.2006	05.07.2006	

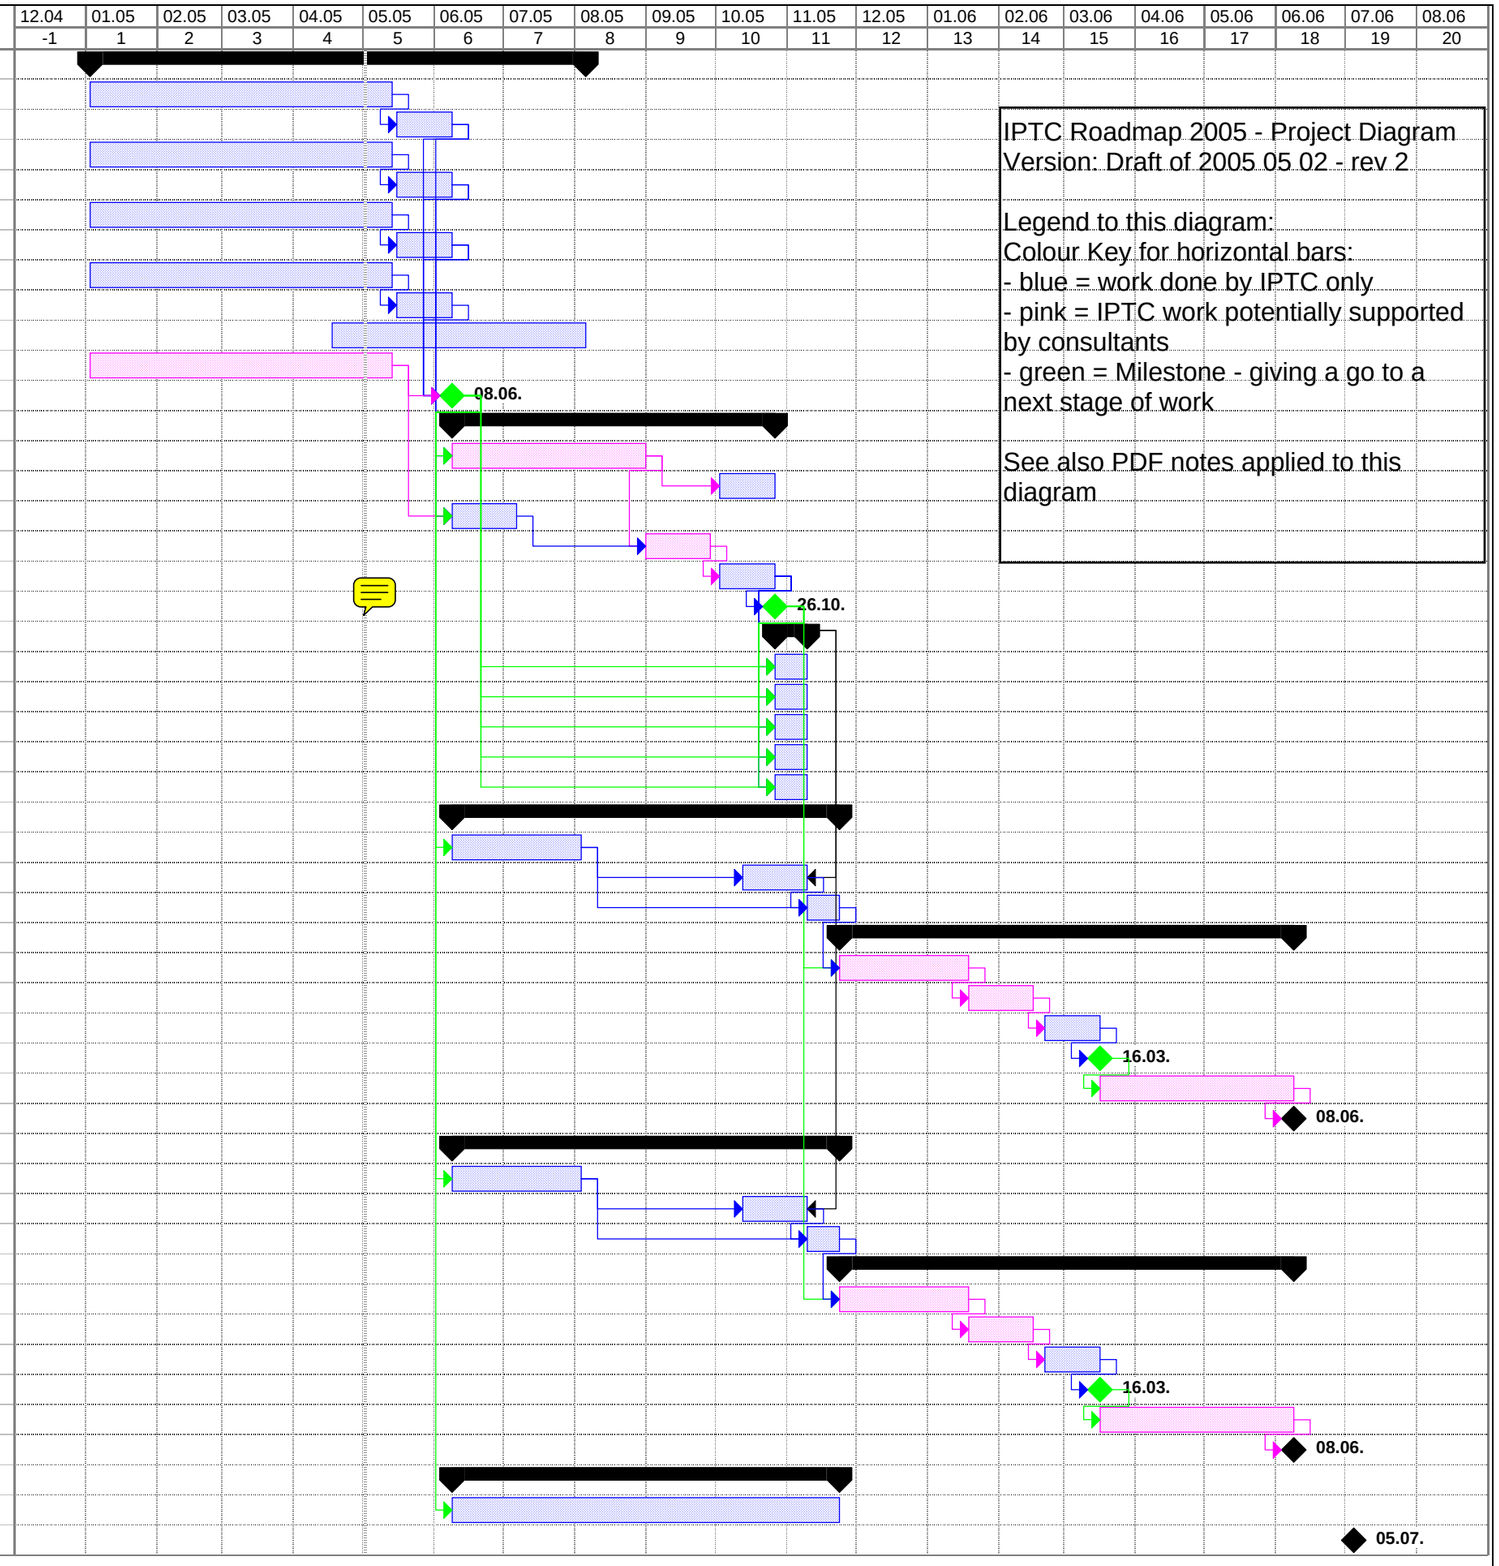

IPTC Roadmap 2005 - Project Diagram
Version: Draft of 2005 05 02 - rev 2

Legend to this diagram:
Colour Key for horizontal bars:
- blue = work done by IPTC only
- pink = IPTC work potentially supported by consultants
- green = Milestone - giving a go to a next stage of work

See also PDF notes applied to this diagram
